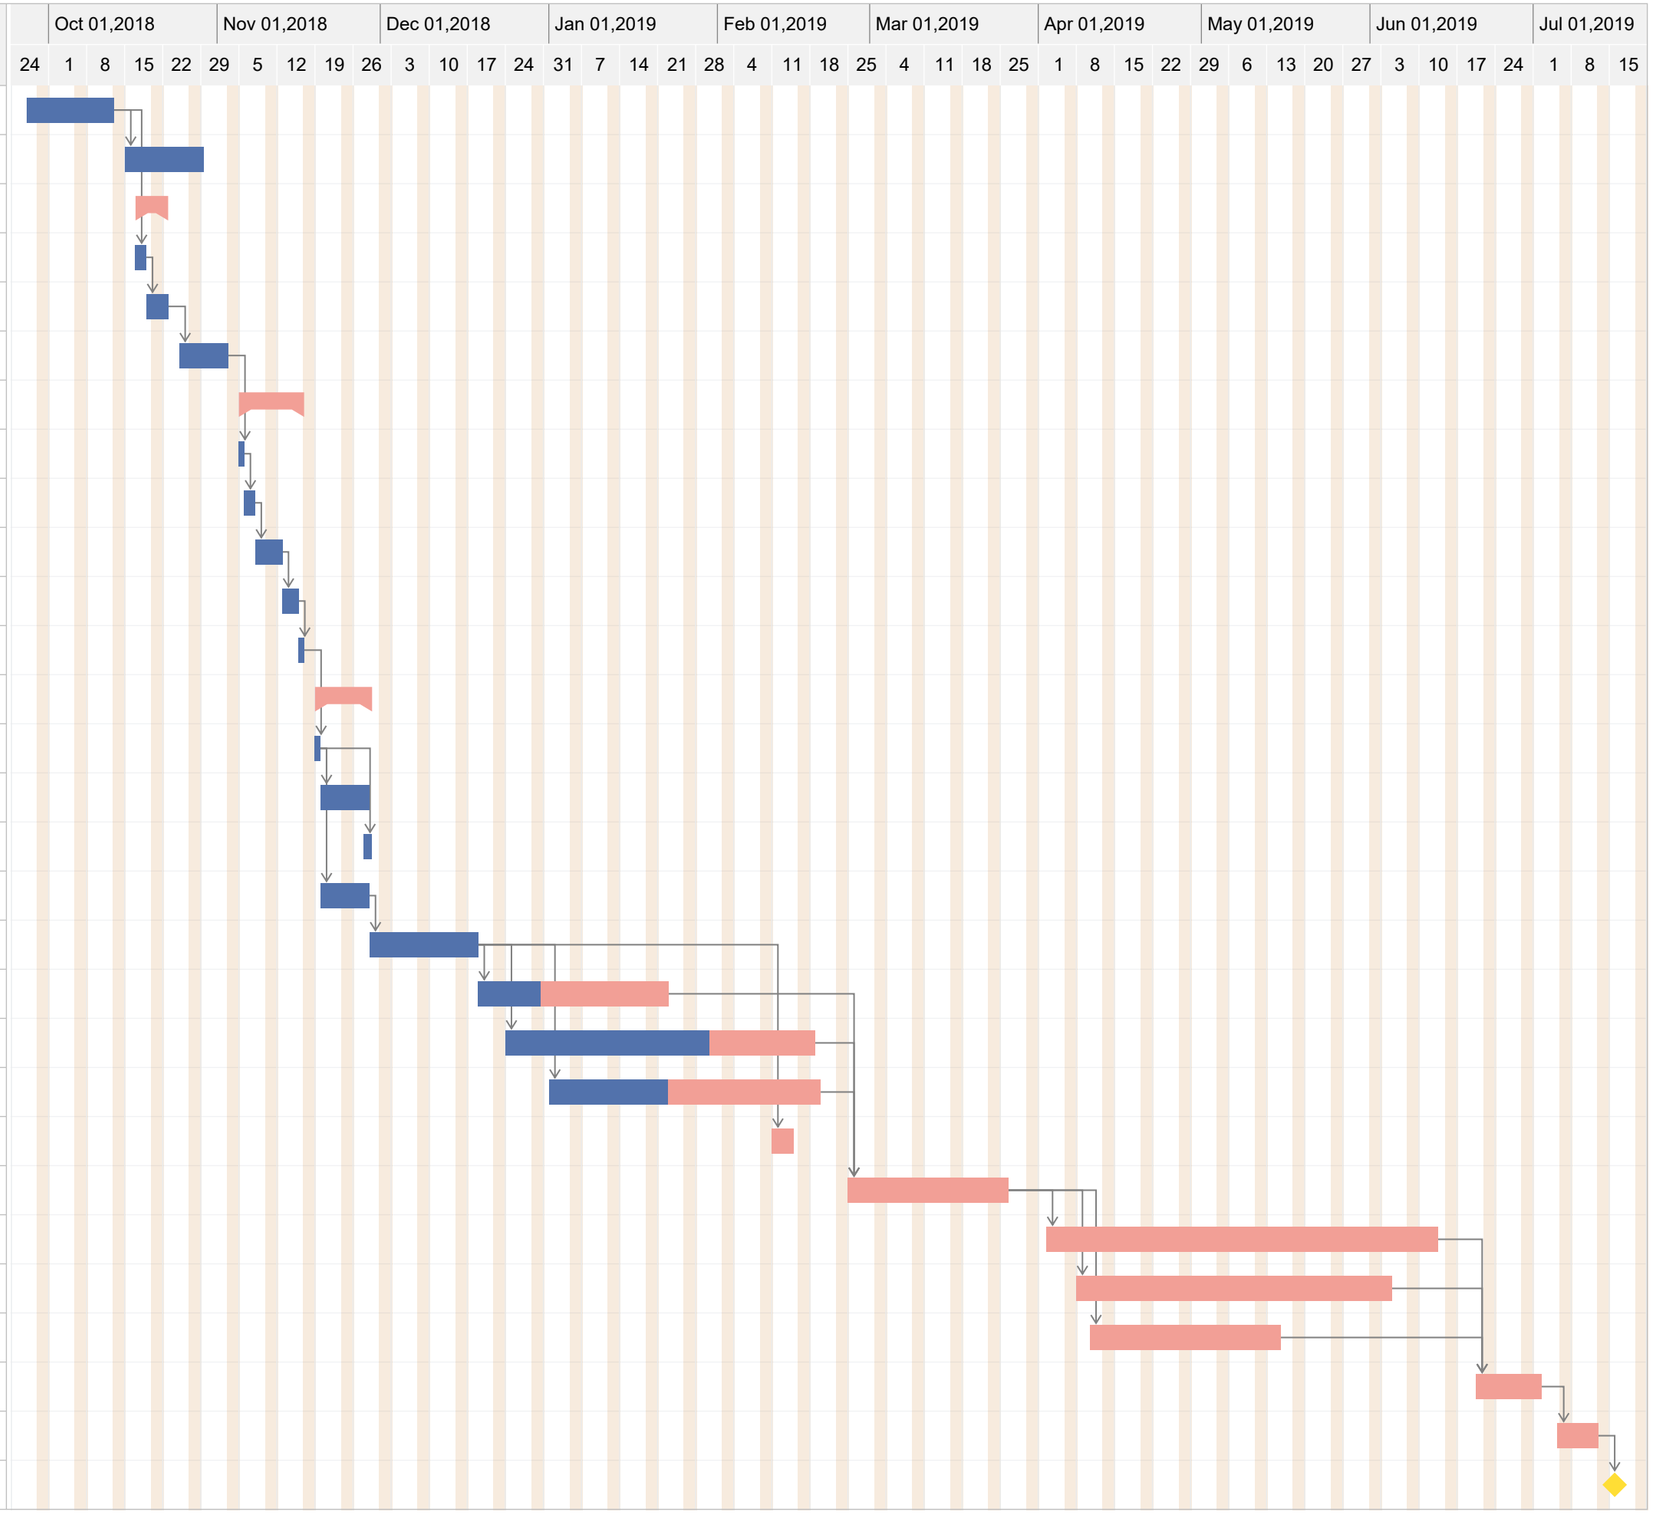ID	Task	Duration	Progress
1	Document Review & Revision	12 d	100%
2	Bids & Contracts	10.5 d	100%
3	Grading & Building Permits	4 d	100%
4	Install Construction Entrance	2 d	100%
5	Install Sediment Controls	2 d	100%
6	Site Work	7 d	100%
7	Foundation	10 d	100%
8	Layout Footings	1 d	100%
9	Install Reinforcing	2 d	100%
10	Build Block Foundation	3 d	100%
11	Materials Delivery	3 d	100%
12	Waterproofing	1 d	100%
13	Rough Carpentry	8.5 d	100%
14	Set Steel	1 d	100%
15	Framing	7 d	100%
16	Install Windows & Doors	1.5 d	100%
17	Concrete Slabs	7 d	100%
18	H.V.A.C.	14 d	100%
19	Facilities Rough-in	25 d	33%
20	Roofing	41 d	66%
21	Finish Exterior Work	36 d	44%
22	Insulation	4 d	0%
23	Drywall	21.5 d	0%
24	Finish Floor	52 d	0%
25	Paint	42 d	0%
26	Exterior Landscaping	25 d	0%
27	Install Hardware	8 d	0%
28	Final Punch-out	5.5 d	0%
29	Construction Close-out	1 d	0%
